

PHASE III

SECTION 1 - -L- STA 465+00 TO STA 650+00, -Y4- AND -Y5

SECTION 2 - -L- FROM STA 650+00 TO STA 915+07, -Y1B-, -Y6- AND -Y7-

- B. 1. BEHIND BARRIER, PLACE THE FOLLOWING FOR THE PHASE IV TRAFFIC PATTERN:
- * FOR THE OUTSIDE SHOULDER OF SB -L-:
 - TEMPORARY ANCHORED PCB FROM STA 495+00+/- TO STA 518+50+/- AS SHOWN ON TMP-81 THRU TMP-83
 - TEMPORARY PCB FROM STA 579+20+/- TO STA 605+00+/- AS SHOWN ON TMP-88 THRU TMP-90
 - TEMPORARY ANCHORED PCB FROM STA 605+00+/- TO STA 627+11+/- AS SHOWN ON TMP-88 THRU TMP-92
 - TEMPORARY ANCHORED PCB FROM STA 634+60+/- TO STA 636+70+/- AS SHOWN ON TMP-93 WITH TEMPORARY ATTACHMENT TO PROPOSED MEDIAN BARRIER
 - * FOR THE OUTSIDE SHOULDER NB -L-:
 - TEMPORARY ANCHORED PCB FROM STA 495+00+/- TO STA 518+50+/- AS SHOWN ON TMP-81 THRU TMP-83
 - TEMPORARY ANCHORED PCB FROM STA 534+18+/- TO STA 561+35+/- AS SHOWN ON TMP-84 THRU TMP-86
 - * FOR THE INSIDE SHOULDER OF SB -L-, PLACE TEMPORARY PCB FROM STA 574+63+/- TO STA 581+00+/- USING A TEMPORARY ATTACHMENT TO THE PROPOSED MEDIAN BARRIER AS SHOWN ON TMP-87 AND TMP-88
- BEHIND BARRIER BEGIN PLACEMENT OF TEMPORARY PAVEMENT MARKINGS FOR THE PHASE IV NB AND SB TEMPORARY TRAFFIC PATTERN AT THE FOLLOWING LOCATIONS
- * NB FROM STA 495+00+/- TO STA 574+00 AS SHOWN ON TMP-81 THRU TMP-87
 - * SB PATTERN FROM STA 495+00+/- TO STA 639+00+/- AS SHOWN ON TMP-81 THRU TMP-93
2. USING RSD 1101.02, SHEET 4 OF 14 AS NEEDED, PERFORM THE FOLLOWING:
- * AT THE MEDIAN CROSSOVER ON -L- (INSIDE SHOULDER OF NB):
 - PLACE TEMPORARY PCB FROM STA 581+00+/- TO STA 582+60+/- AS SHOWN ON TMP-88
 - RESET TEMPORARY ANCHORED PCB FROM STA 582+60+/- TO STA 583+56+/- AS SHOWN ON TMP-88
 - * REMOVE TEMPORARY ANCHORED PCB ON THE INSIDE SHOULDER OF NB -L- FROM STA 581+00+/- TO STA 582+60+/- AS SHOWN ON TMP-88
 - * REMOVE TEMPORARY PCB FROM THE INSIDE SHOULDER OF SB -L- FROM STA 638+00+/- TO STA 645+50+/- TMP-76 AND TMP-77 AND RESET CRASH CUSHION
3. USING RSD 1101.02, SHEET 4 OF 14 AS NEEDED, PERFORM THE FOLLOWING:
- * REMOVE TEMPORARY ANCHORED AND TEMPORARY PCB FROM THE INSIDE SHOULDER OF SB -L- FROM STA 521+41+/- TO STA 579+50+/- AND PLACE DRUMS TO MAINTAIN PHASE II TRAFFIC PATTERN (TMP-66 THRU TMP-71)
 - * REMOVE TEMPORARY ANCHORED PCB FROM THE INSIDE SHOULDER OF NB -L- FROM STA 561+35+/- TO STA 581+00+/- (TMP-69 THRU TMP-71)
 - * REMOVE TEMPORARY PCB ON OUTSIDE SHOULDER OF SB -L- FROM STA 642+70+/- TO STA 650+00+/- (TMP-76 AND TMP-77)

END PHASE III, SECTION 1


3/29/2022 G:\50100191\NV5_1-5987B\TrafficControl\Twp\200_085_1-5987B-TMP-3R-Phase III.220315.dgn User:ST086227

PLANS PREPARED FOR THE NCDOT BY:

M MOTT MACDONALD I & E, LLC
1101 HAYNES STREET, SUITE 101
RALEIGH, NC 27604


M MOTT MACDONALD NC LICENSE NO. F-0669

APPROVED: *Lori D. Stoucho*
4/29/2022



DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED


APPROVED: *J.W. Woolard, Jr.*
4/29/2022



DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED



Stantec Consulting Services Inc.
801 Jones Franklin Road
Suite 300
Raleigh, NC 27606
Tel. 919.851.6866
Fax. 919.851.7024
www.stantec.com
License No. F-0672

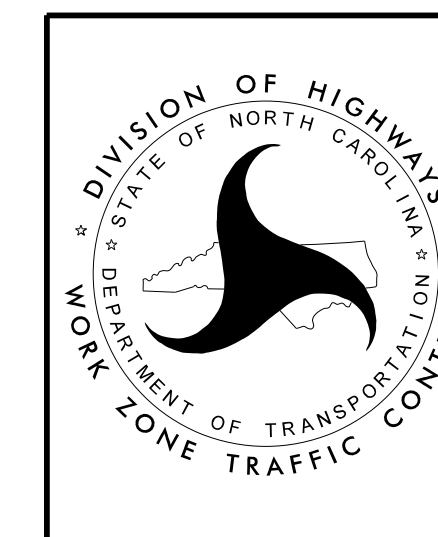

TEMPORARY TRAFFIC CONTROL PHASING PHASE III
