PROJECT REFERENCE NO.	SHEET NO.
U-4751	EC-14A/CONST14
R/W SHEET NO.	___

STV 100 Years
STV Engineers, Inc.
900 West Trade St., Suite 715
Charlotte, NC 28202
NC License Number F-0991

CULVERT CONSTRUCTION SEQUENCE STA. 138 + 59 –L–

PHASE I

1. INSTALL SPECIAL STILLING BASIN AS DIRECTED.
2. CONSTRUCT IMPERVIOUS DIKE, DEWATER CULVERT CONSTRUCTION AREA.
3. CONSTRUCT PROPOSED CULVERT AND WESTERN INLET/OUTLET CHANNEL IMPROVEMENTS.

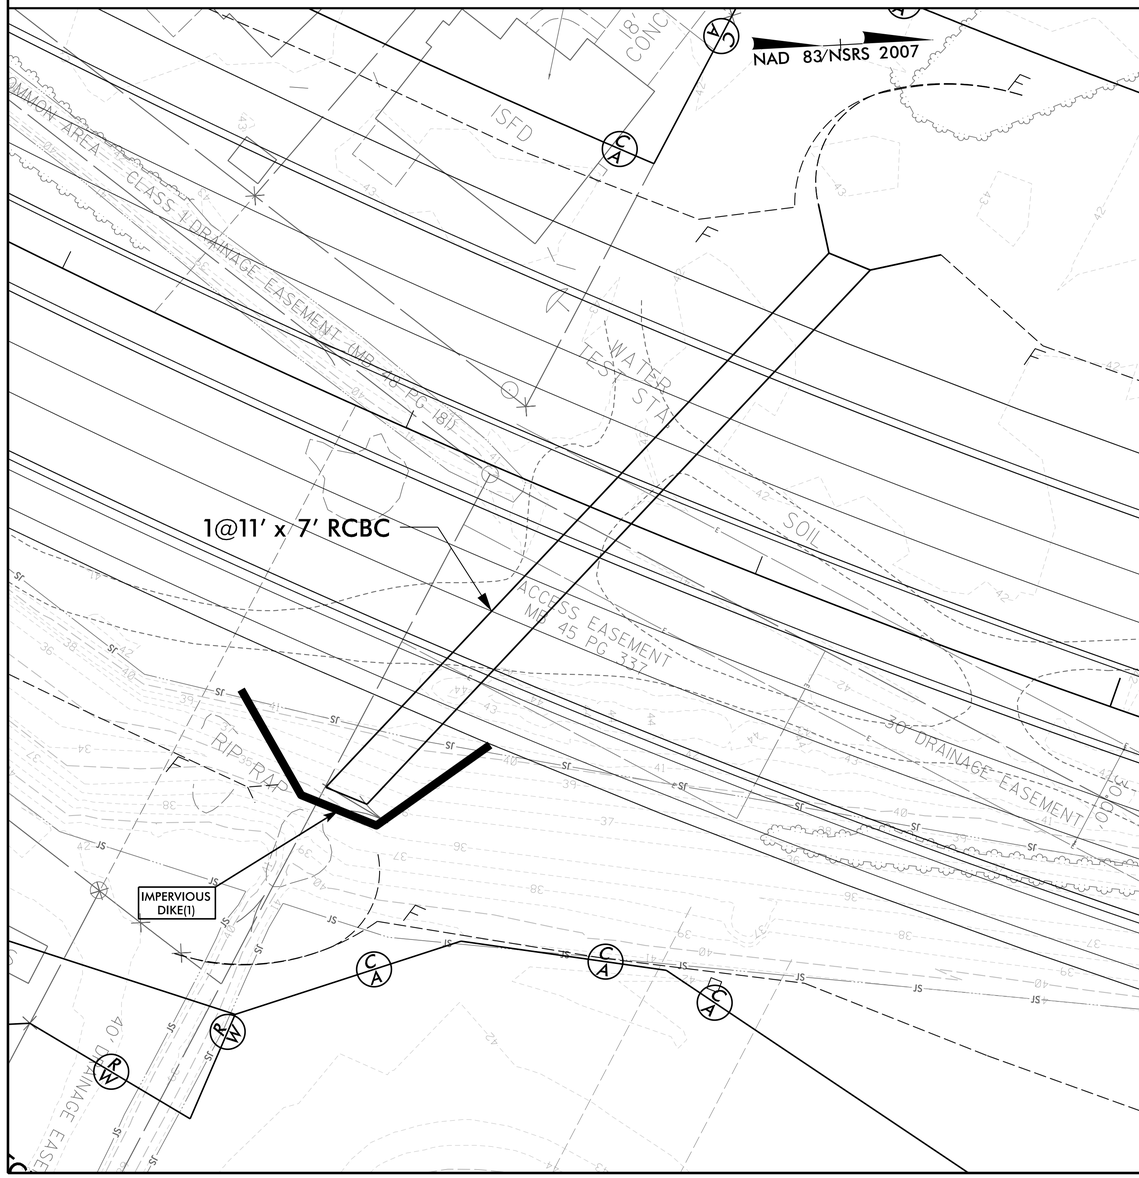

PHASE II
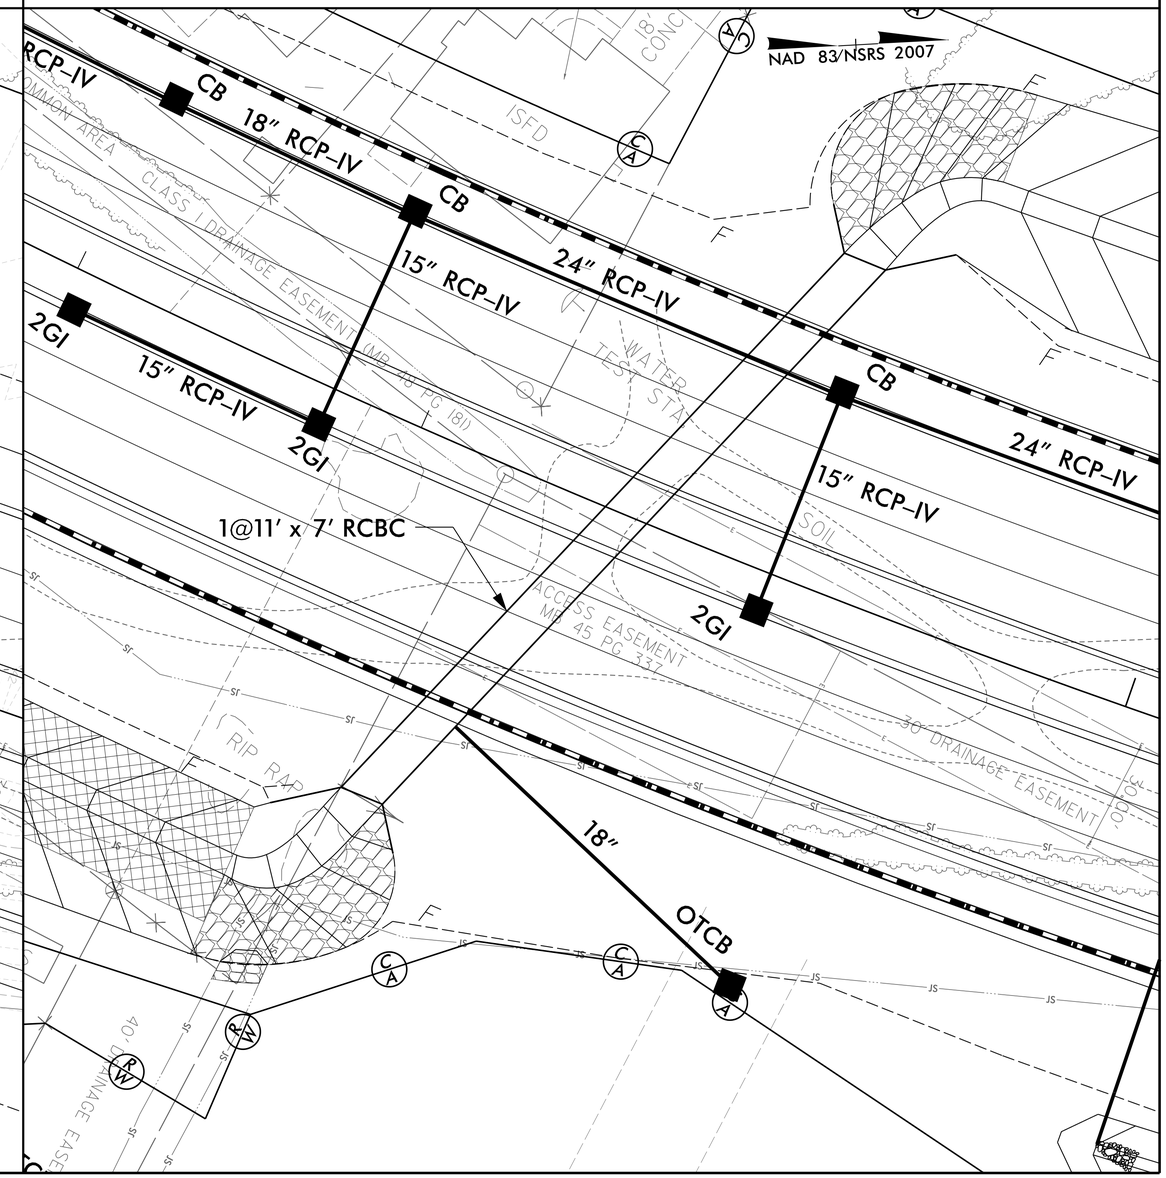
4. CONSTRUCT PROPOSED STREAM RELOCATION.
5. EXCAVATE ANY ACCUMULATED SILT AND DEWATER BEFORE REMOVAL OF IMPERVIOUS DIKE.
6. REMOVE IMPERVIOUS DIKE, DIVERTING FLOW THROUGH PROPOSED CULVERT.
7. CONSTRUCT EASTERN INLET CHANNEL IMPROVEMENTS.
8. REMOVE SPECIAL STILLING BASIN, STABILIZE DISTURBED AREA, AND COMPLETE ROADWAY.
