


PROJ. REFERENCE NO.	SHEET NO.
BR-0119	TMP-1A

**KCA** 301 FAYETTEVILLE STREET  
 SUITE 1500  
 RALEIGH, NC 27601  
 (919) 882-7839  
**KISINGER CAMPO & ASSOCIATES** NC FIRM LICENSE: C-1506

## LEGEND

### GENERAL

 NORTH ARROW

### TRAFFIC CONTROL DEVICES

 BARRICADE (TYPE III)

### TEMPORARY SIGNING

 STATIONARY SIGN

## GENERAL NOTES

CHANGES MAY BE REQUIRED WHEN PHYSICAL DIMENSIONS IN THE DETAIL DRAWINGS, STANDARD DETAILS, AND ROADWAY DETAILS ARE NOT ATTAINABLE TO MEET FIELD CONDITIONS OR RESULT IN DUPLICATE OR UNDESIRABLE OVERLAPPING OF DEVICES. MODIFICATION MAY INCLUDE: MOVING, SUPPLEMENTING, COVERING, OR REMOVAL OF DEVICES AS DIRECTED BY THE ENGINEER.

THE FOLLOWING GENERAL NOTES APPLY AT ALL TIMES FOR THE DURATION OF THE CONSTRUCTION PROJECT EXCEPT WHEN OTHERWISE NOTED IN THE PLAN OR DIRECTED BY THE ENGINEER.

### TRAFFIC PATTERN ALTERATIONS

A) NOTIFY THE ENGINEER THIRTY (30) CALENDAR DAYS PRIOR TO ANY TRAFFIC PATTERN ALTERATION.

### SIGNING

B) INSTALL ADVANCE WORK ZONE WARNING SIGNS WHEN WORK IS WITHIN 40 FT FROM THE EDGE OF TRAVEL LANE AND NO MORE THAN THREE (3) DAYS PRIOR TO THE BEGINNING OF CONSTRUCTION.

C) PROVIDE SIGNING AND DEVICES REQUIRED TO CLOSE THE ROAD ACCORDING TO THE ROADWAY STANDARD DRAWINGS AND TRAFFIC CONTROL PLANS.

PROVIDE SIGNING REQUIRED FOR THE OFF-SITE DETOUR ROUTE AS SHOWN IN THE TRAFFIC CONTROL PLANS.

D) COVER OR REMOVE ALL SIGNS AND DEVICES REQUIRED TO CLOSE THE ROAD WHEN ROAD CLOSURE IS NOT IN OPERATION.

COVER OR REMOVE ALL SIGNS REQUIRED FOR THE OFF-SITE DETOUR WHEN THE DETOUR IS NOT IN OPERATION.

E) ENSURE ALL NECESSARY SIGNING IS IN PLACE PRIOR TO ALTERING ANY TRAFFIC PATTERN.

### TRAFFIC CONTROL DEVICES

F) PLACE TYPE III BARRICADES, WITH "ROAD CLOSED" SIGN R11-2 ATTACHED, OF SUFFICIENT LENGTH TO CLOSE ENTIRE ROADWAY.

### ADDITIONAL NOTES

G) ACCESS WILL BE MAINTAINED THROUGHOUT CONSTRUCTION FOR THE ADJACENT PROPERTIES, THE DIRT ROAD, AND THE DRAINAGE DISTRICT ACCESS DRIVES AND GATES LOCATED NORTH OF THE BRIDGE.

H) PITT COUNTY EMERGENCY SERVICES SHALL BE CONTACTED (252) 902-3950 AT LEAST ONE MONTH PRIOR TO CONSTRUCTION TO MAKE NECESSARY TEMPORARY REASSIGNMENTS TO PRIMARY RESPONSE UNITS.

## PHASING NOTES

### PHASE I

#### STEP 1

PRIOR TO ANY CONSTRUCTION OPERATIONS, PLACE AND COVER OFF-SITE DETOUR SIGNS FOR WHICHARD RD (SR 1523), NC 903, OAKLEY RD (SR 1517), SWEET GUM GROVE CHURCH RD (SR 1521), TETTERTON RD (SR 1520), STATON MILL RD. (SR 1514), AS SHOWN ON TMP-2, AND IN ACCORDANCE WITH RSD 1101.03 (SHEETS 1 OF 9).

#### STEP 2


USING OFF-SITE DETOUR, AS SHOWN ON TMP-2, UNCOVER DETOUR SIGNS, CLOSE -L- (SR 1514 / STATON MILL RD) TO TRAFFIC AND CONSTRUCT PROPOSED BRIDGE AND ROADWAY UP TO AND INCLUDING THE FINAL LAYER OF SURFACE COURSE PER ROADWAY AND BRIDGE PLANS.


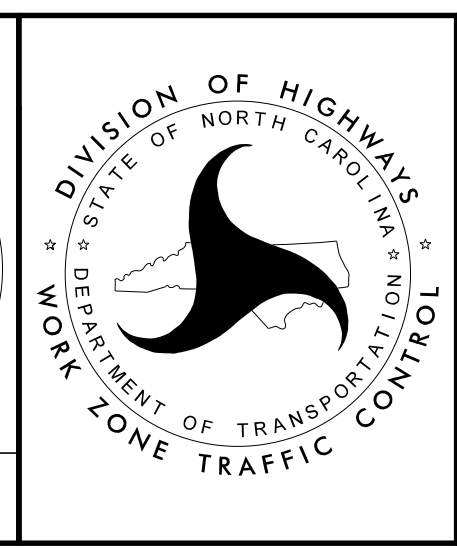
#### STEP 3

UPON COMPLETION OF BRIDGE AND ROADWAY CONSTRUCTION, PLACE FINAL PAVEMENT MARKINGS AND MARKERS IN ACCORDANCE WITH RSD 1205.01, 1205.02, 1205.12, 1250.01, 1251.01, AND PAVEMENT MARKING PLANS. REMOVE ALL SIGNS AND DEVICES, AND OPEN -L- (SR 1514 / STATON MILL RD) TO TRAFFIC.

2/6/2020  
BR-019\_TC\_TMP\_LEGEND-GEN\_NOTES-PHASING.dgn  
User: jdebbon

APPROVED: \_\_\_\_\_  
 DATE: \_\_\_\_\_  
 2/6/2020

Decoded by:  
  
 SC053AD086D6400...

LEGEND, GENERAL NOTES,  
 AND PHASING NOTES

**DOCUMENT NOT CONSIDERED FINAL  
UNLESS ALL SIGNATURES COMPLETED**
