

PHASE III

AREA I



PROJ. REFERENCE NO.	SHEET NO.
R-2206C	TCP-6

NOTE: THE CONTRACTOR SHALL NOT CLOSE -Y11- (FORNEY HILL ROAD) AND -Y13- (MUNDY ROAD) SIMULTANEOUSLY.

STEP 1. INSTALL ALL OFFSITE DETOUR SIGNING (SEE TCP-7) FOR FORNEY HILL RD. (SR 1373). REMOVE ADVANCE WARNING SIGNS FROM PHASE I, STEP 1.

THE CONTRACTOR SHALL COMPLETE THE WORK REQUIRED OF PHASE III, STEPS 2 THRU 5 IN 30 CONSECUTIVE CALENDER DAYS. (SEE INTERMEDIATE CONTRACT TIME AND LIQUIDATED DAMAGES).

STEP 2. USING TCP-7 AND RSD NO. 1101.03 (SHEET 1 OF 9), CLOSE FORNEY HILL ROAD (SR 1373) FROM STA. 10+00 +/- -Y11- TO STA. 15+80 +/- -Y11-.

MAINTAIN ACCESS TO ALL DRIVEWAYS WITHIN PROJECT LIMITS.


STEP 3. CONSTRUCT -Y11- TIE-INS FROM STA. 10+00 +/- TO STA. 11+50 +/- AND FROM STA. 13+80 +/- TO STA. 15+80 +/-, INCLUDING DRAINAGE, UP TO BUT NOT INCLUDING FINAL LAYER OF SURFACE COURSE.

STEP 4. PLACE FINAL LAYER OF SURFACE COURSE AND FINAL PAVEMENT MARKINGS AND MARKERS ON -Y11- FROM STA. 10+00 +/- TO STA. 15+80 +/- . REFER TO RSD NOS. 1205.01, 1205.02, 1205.12, 1250.01, AND 1251.01. FOR FINAL PAVEMENT SCHEDULE, SEE PM-1.

OBLITERATE REMAINING -Y11DET- PAVEMENT.

STEP 5. REMOVE ALL TYPE III BARRICADES, DRUMS, AND ALL DETOUR SIGNING. REOPEN SR 1373 (FORNEY HILL RD.) TO 2-LANE, TWO-WAY TRAFFIC.

STEP 6. CONTINUE -L- LINE CONSTRUCTION FROM STA. 195+70 +/- TO STA. 196+30 +/-, INCLUDING DRAINAGE.

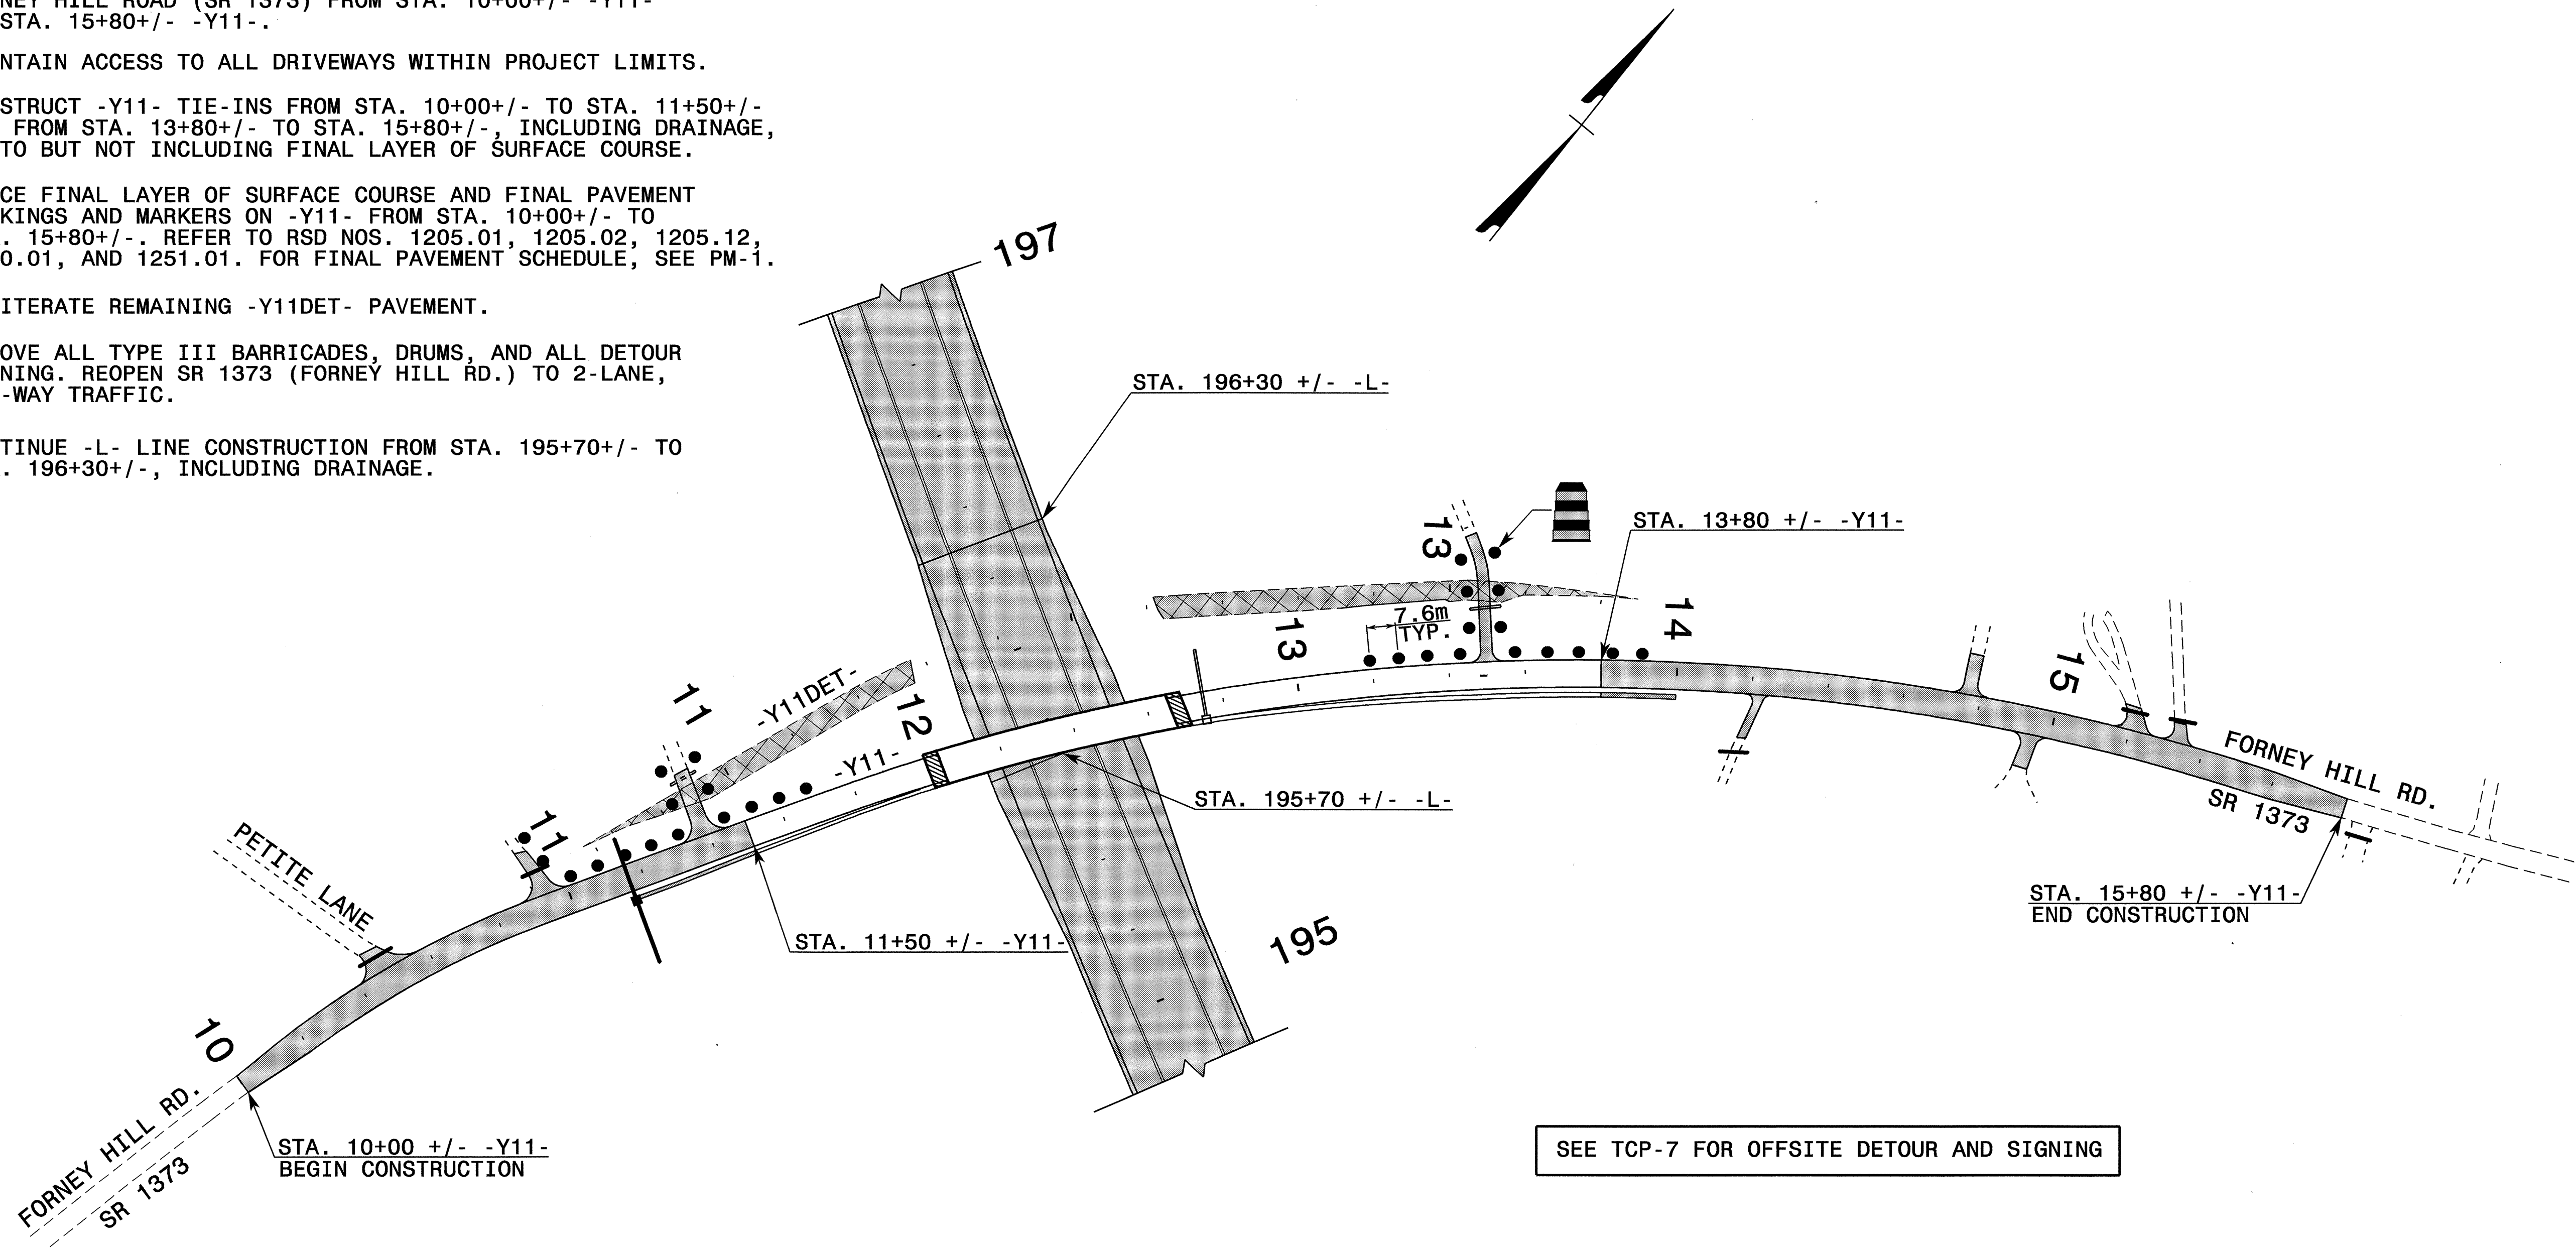

SEE TCP-7 FOR OFFSITE DETOUR AND SIGNING

09-JUL-2004 14:25 J:\TCP\AREA\YR2206C.TC\AREAL.TCP06.dgn SBC\DTIS AT TET206428

APPROVED: DATE: 7/12/04 	AREA 1 PHASE III DETAILS AND PHASING	<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <th colspan="2">REVISIONS</th> </tr> <tr> <td style="width: 50%;"> </td> <td style="width: 50%;"> </td> </tr> <tr> <td> </td> <td> </td> </tr> <tr> <td> </td> <td> </td> </tr> </table>	REVISIONS							
REVISIONS										
SCALE: 1:1000 DATE: 05-10-04 DWG. BY: SBC DESIGN BY: SBC REVIEWED BY: CLM		<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 50%;">CAD</td> <td style="width: 50%;">FILE</td> </tr> </table>	CAD	FILE						
CAD	FILE									
