

-L- CONSTRUCTION

1. AWAY FROM TRAFFIC, BEGIN CONSTRUCTION OF -L- LINE, INCLUDING GRADING, DRAINAGE, AND STRUCTURES FROM:

- STA. 180+67 +/- TO STA. 195+70 +/- -L-
- STA. 196+30 +/- TO STA. 216+20 +/- -L-
- STA. 216+70 +/- TO STA. 237+58 +/- -L-
- STA. 10+00 +/- TO STA. 15+31 +/- RAMP -A-
- STA. 10+00 +/- TO STA. 14+84 +/- RAMP -B-
- STA. 10+00 +/- TO STA. 14+69 +/- RAMP -C-
- STA. 10+00 +/- TO STA. 14+96 +/- RAMP -D-
- STA. 238+17 +/- TO STA. 267+36 +/- -L-
- STA. 267+36 +/- TO STA. 268+60 +/- -SBL-
- STA. 10+00 +/- TO STA. 11+25 +/- -NBL-
- STA. 11+60 +/- TO STA. 14+08 +/- -Y16-
- STA. 10+00 +/- TO STA. 10+60 +/- -Y17-


FOR INSTALLATION OF TRAFFIC CONTROL DEVICES TO BE LEFT IN PLACE AT COMPLETION OF PROJECT ON -SBL-, -NBL-, -Y16-, AND -Y17- SEE TCP-3A.

AREA OVERVIEW

AREAS 1 THRU 4 ARE INDEPENDENT SITES. FOR CONSTRUCTION PHASING OF EACH AREA, SEE APPROPRIATE AREA PHASING TCP SHEETS.



PROJ. REFERENCE NO.	SHEET NO.
R-2206C	TCP-3

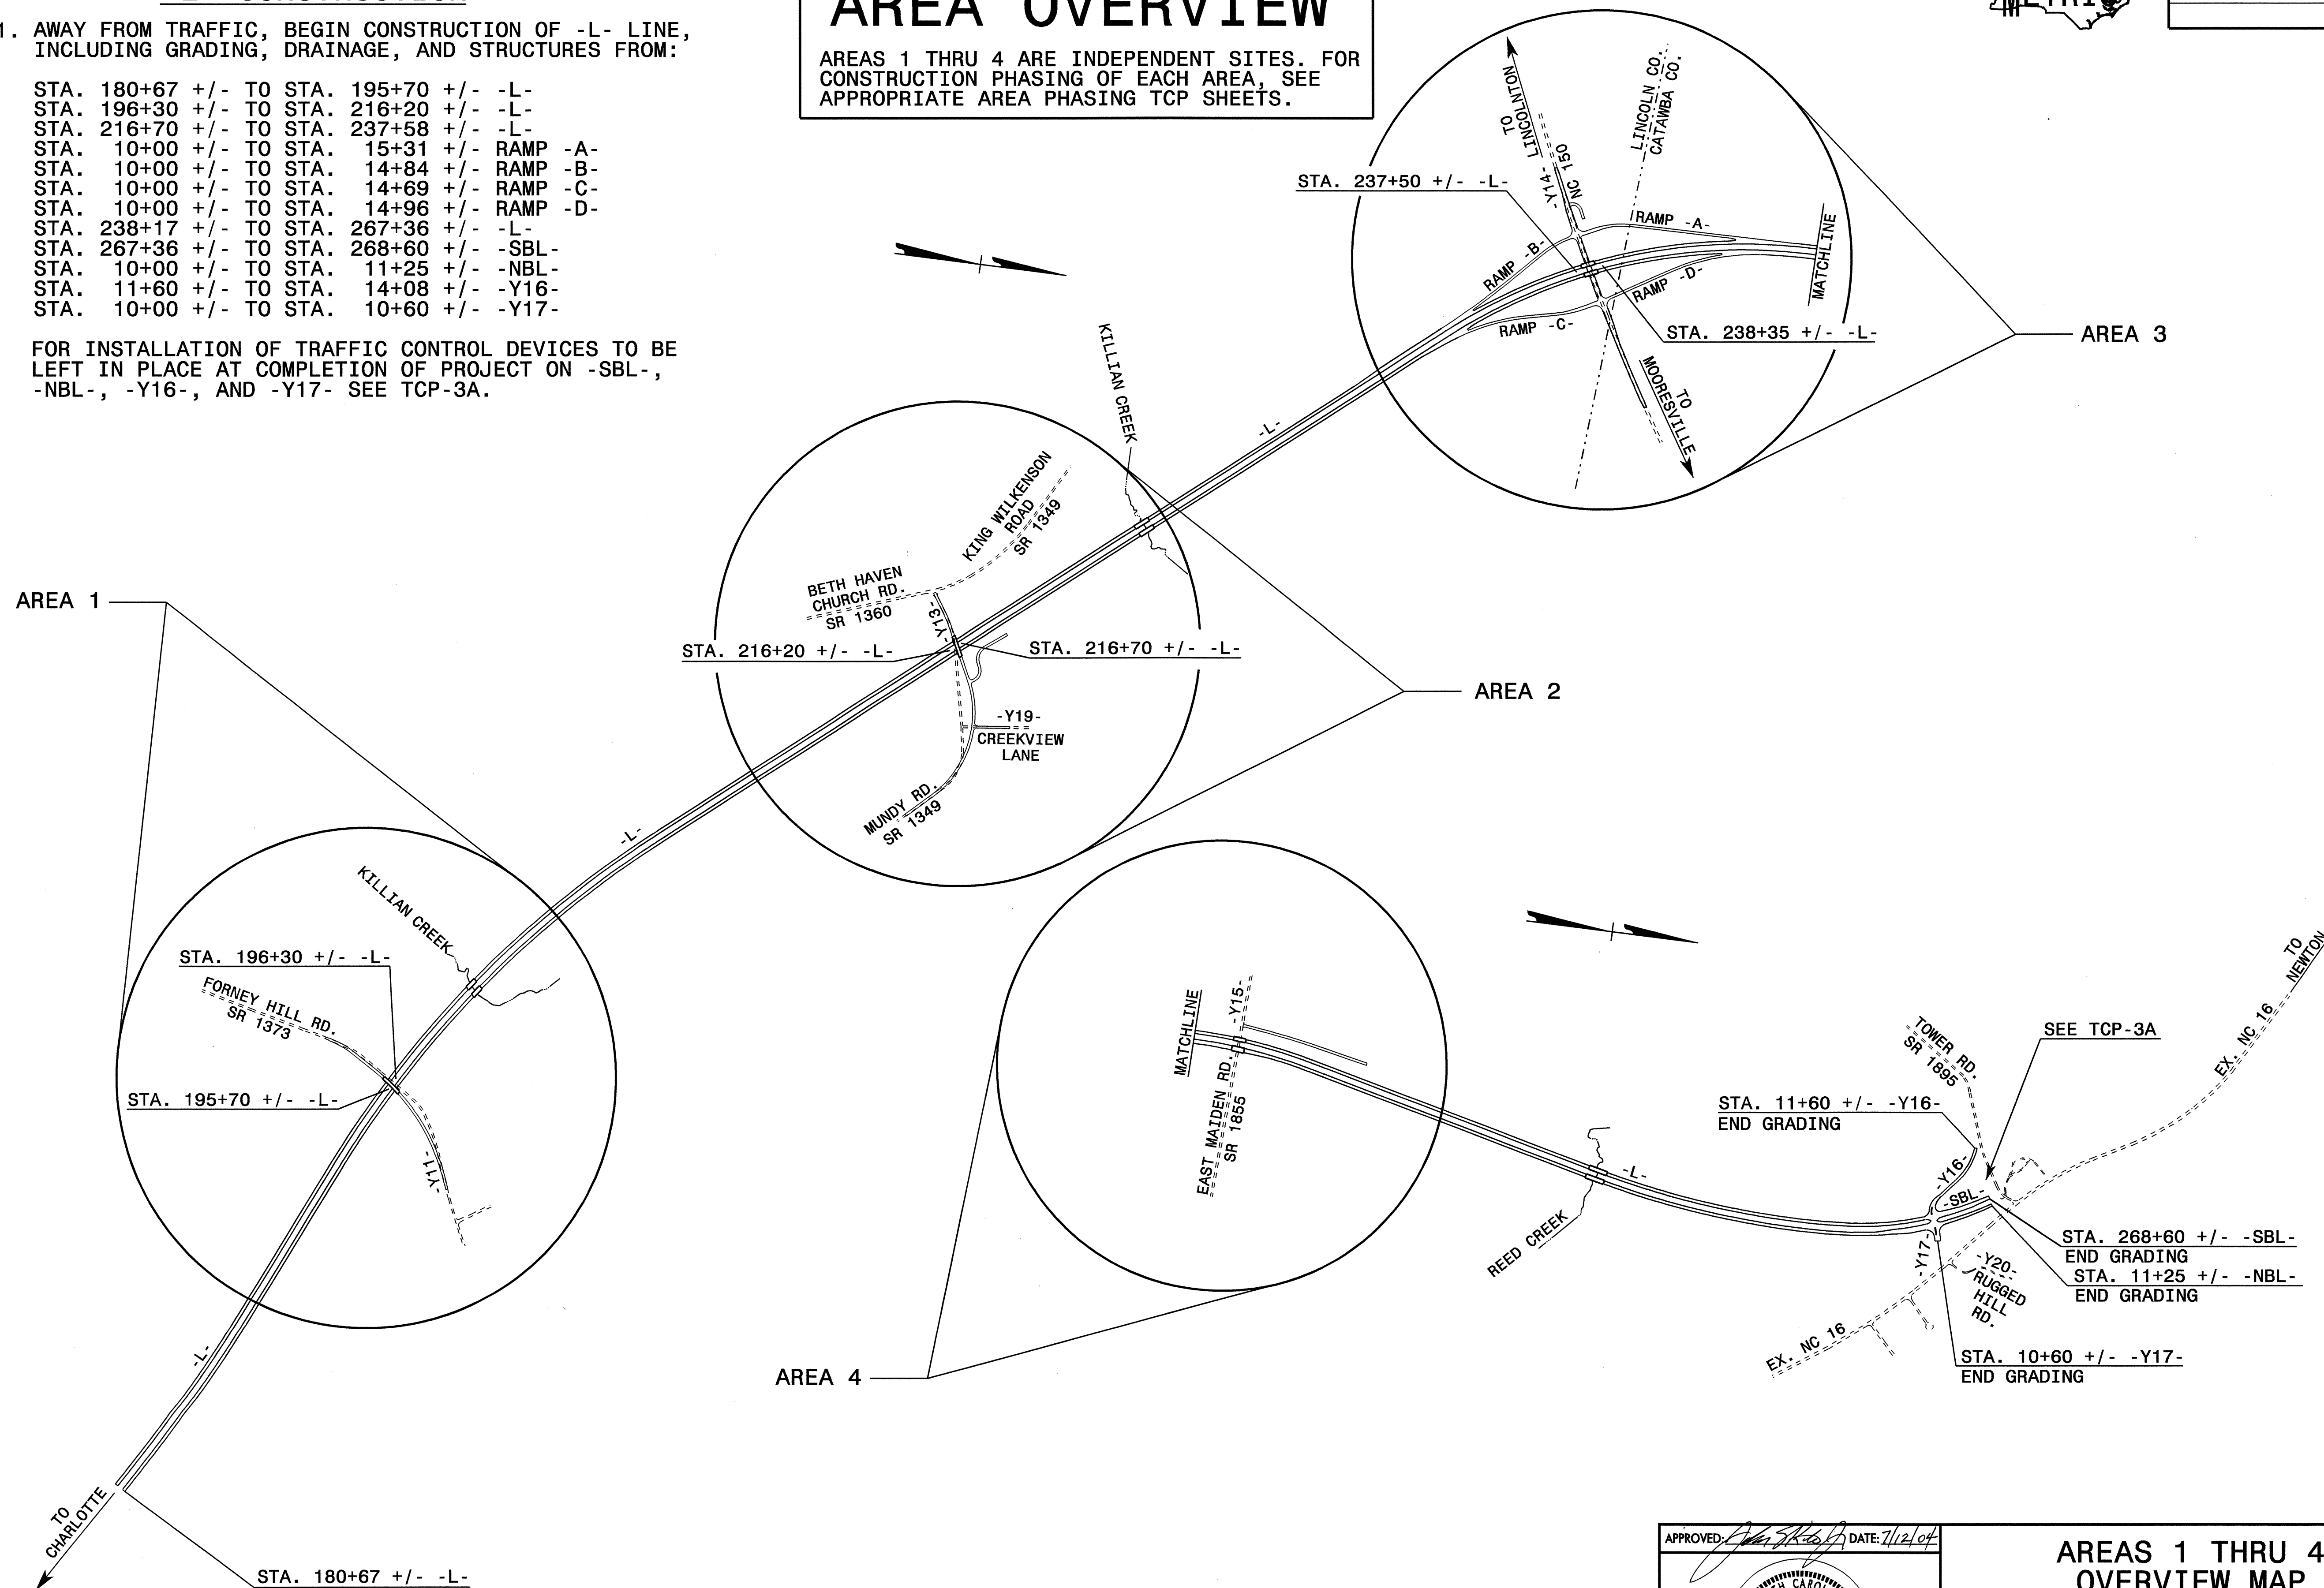

09-JUL-2004 14:24
 J:\TCP\2206C\1\111206428
 S:\scottis AT 111206428

APPROVED: SEAL 	DATE: 7/12/04		AREAS 1 THRU 4 OVERVIEW MAP								
	SCALE: NONE	DATE: 05-10-04			REVISIONS <table border="1"> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> <tr><td> </td><td> </td></tr> </table>						
DWG. BY: SBC	DESIGN BY: SBC	REVIEWED BY: CLM									
