


MATCH LINE D, SEE SHEET 2K

MATCH LINE C, SEE SHEET 2L

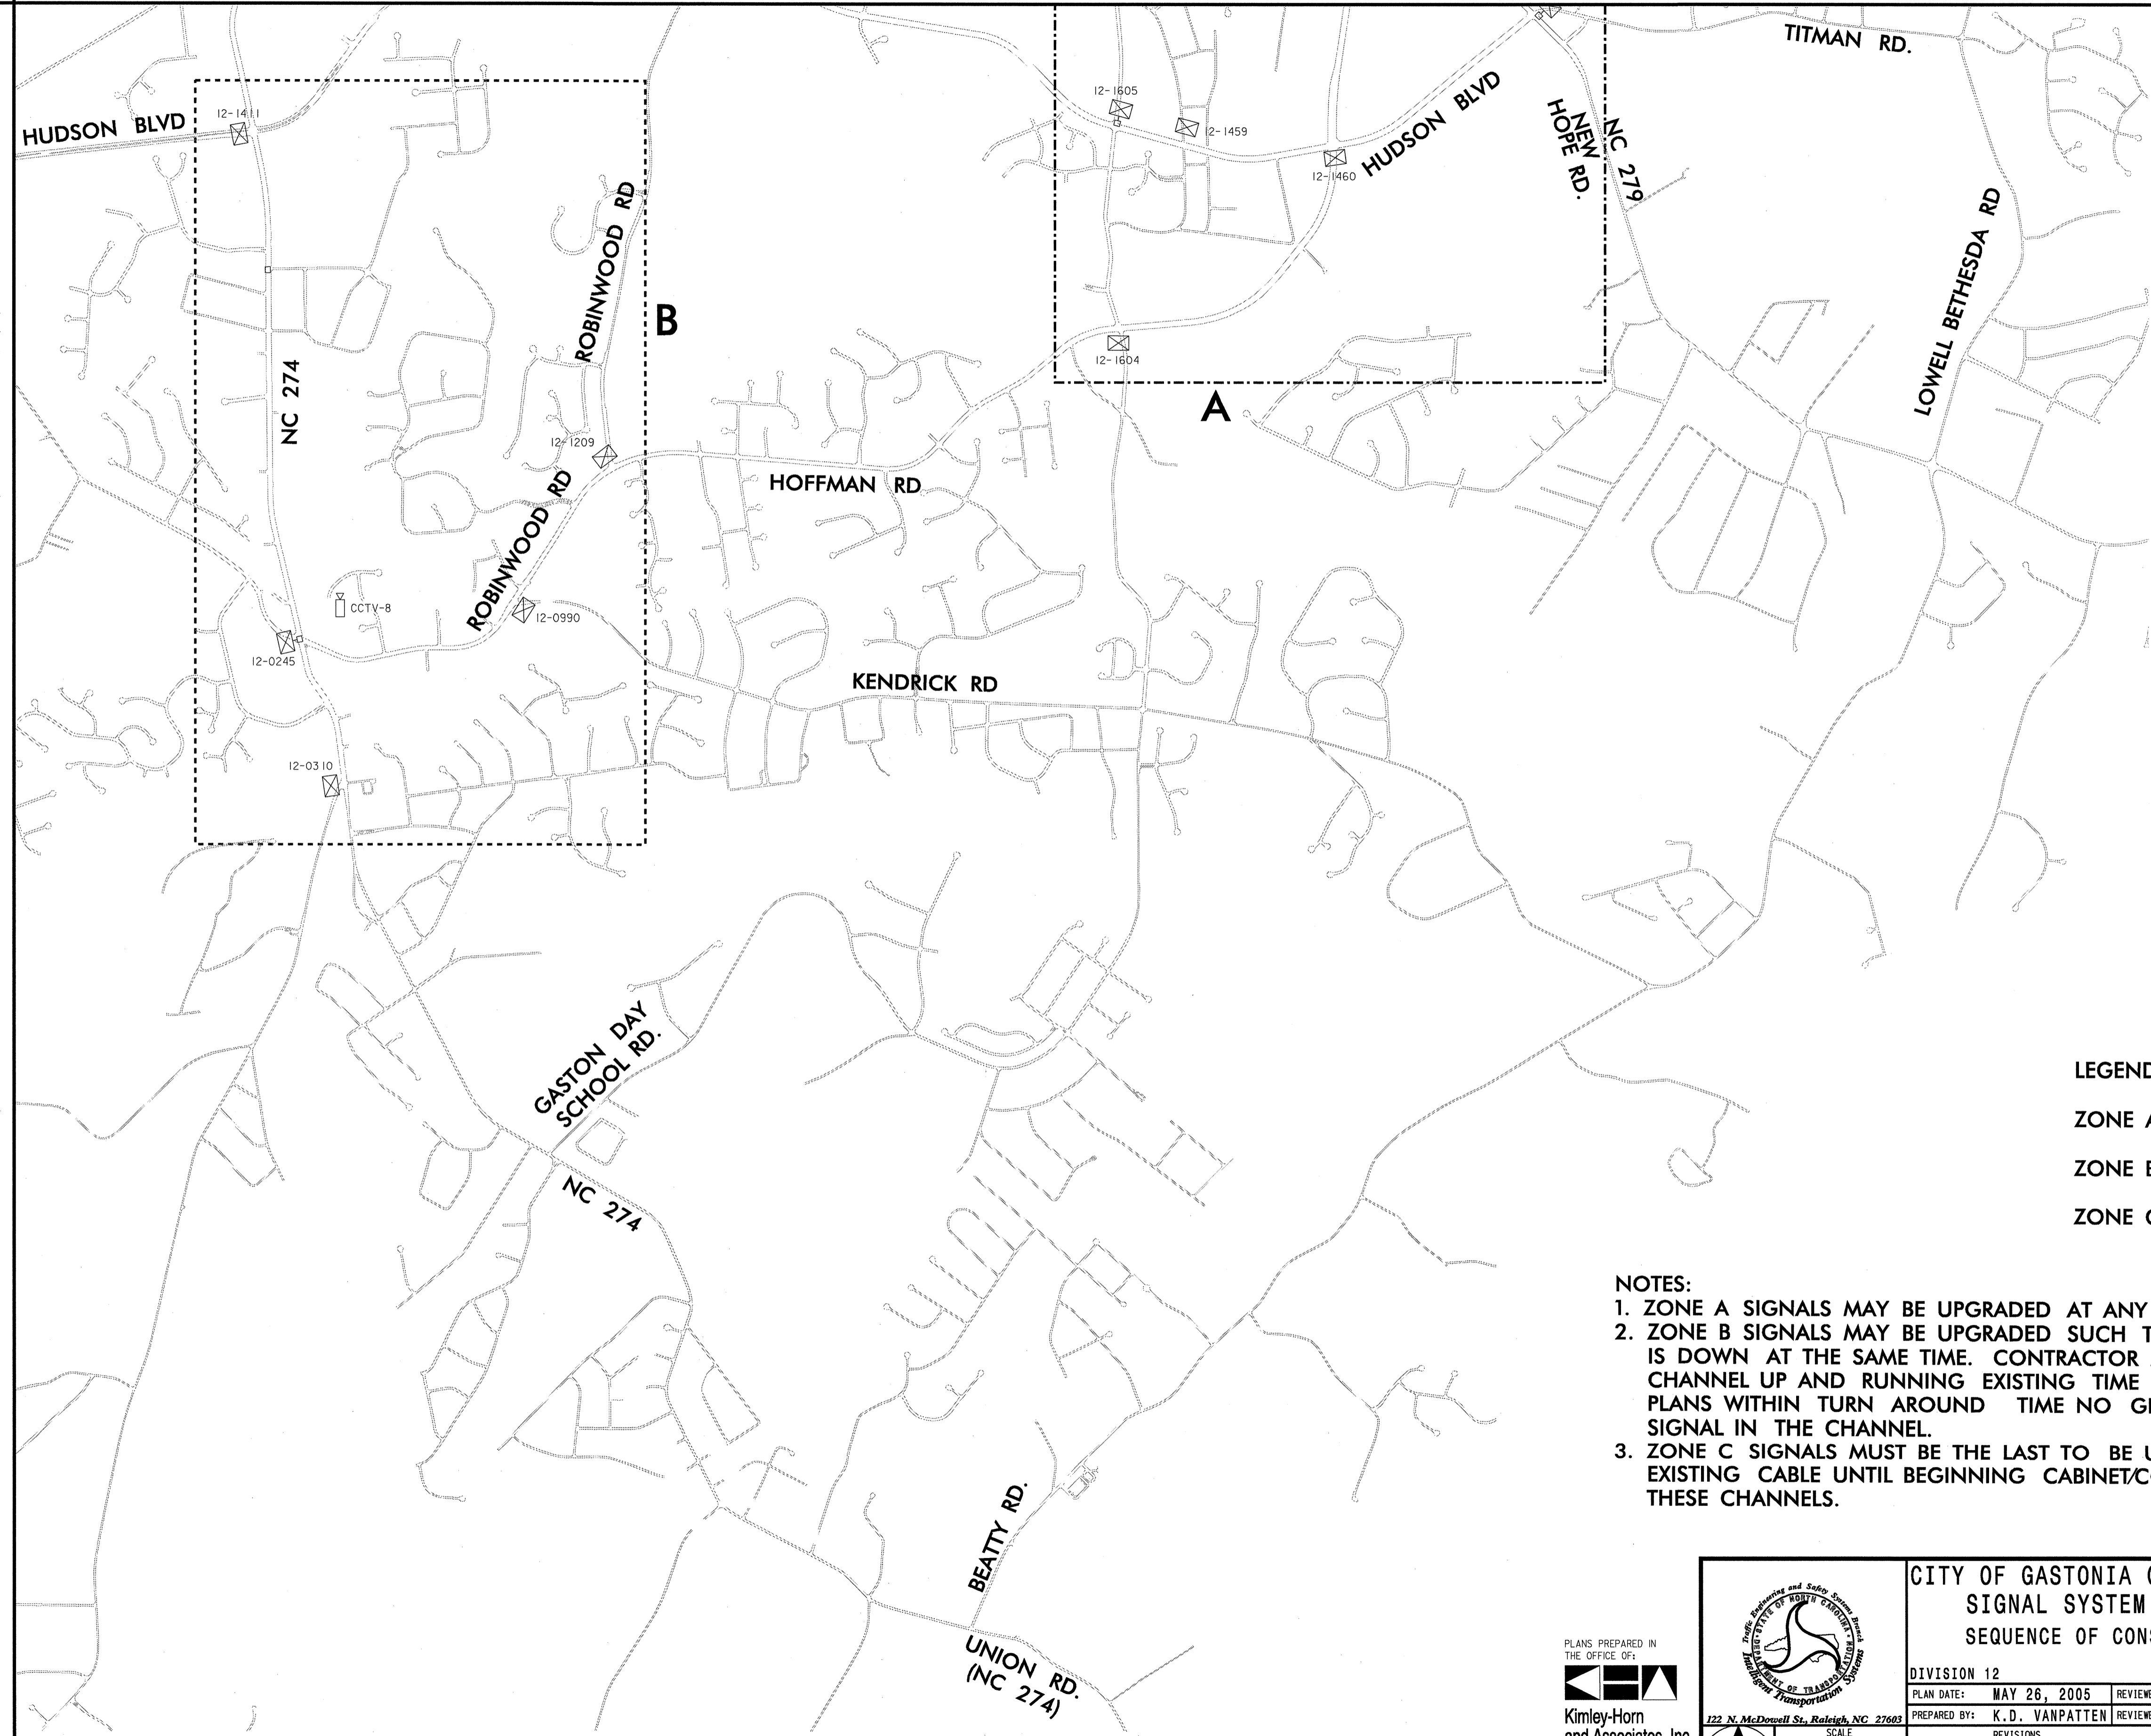


**LEGEND:**  
 ZONE A BOUNDARY - - - - -  
 ZONE B BOUNDARY - - - - -  
 ZONE C BOUNDARY - - - - -

**NOTES:**  
 1. ZONE A SIGNALS MAY BE UPGRADED AT ANY TIME.  
 2. ZONE B SIGNALS MAY BE UPGRADED SUCH THAT ENTIRE CHANNEL IS DOWN AT THE SAME TIME. CONTRACTOR MUST HAVE COMMUNICATION CHANNEL UP AND RUNNING EXISTING TIME OF DAY COORDINATED TIMING PLANS WITHIN TURN AROUND TIME NO GREATER THAN 2 DAYS PER SIGNAL IN THE CHANNEL.  
 3. ZONE C SIGNALS MUST BE THE LAST TO BE UPGRADED. DO NOT CUT EXISTING CABLE UNTIL BEGINNING CABINET/CONTROLLER UPGRADES ON THESE CHANNELS.

05/26/2005  
 T:\systems\proj\1036097\gastonia\shf002.mxd

PLANS PREPARED IN THE OFFICE OF:  
  
**Kimley-Horn and Associates, Inc.**  
 P.O. Box 33068  
 Raleigh, N.C. 27636-3068  
 (919) 677-2000



<b>CITY OF GASTONIA COMPUTERIZED SIGNAL SYSTEM UPGRADE SEQUENCE OF CONSTRUCTION</b>	
DIVISION 12	GASTON COUNTY
PLAN DATE: MAY 26, 2005	REVIEWED BY: I.Z. VANOSDELL
PREPARED BY: K.D. VANPATTEN	REVIEWED BY: M.W. DUNZO
REVISIONS	INIT. DATE

SEAL  
  
 SEAL 023562  
 ENGINEER  
 MARK DUNZO  
 SIGNATURE: *Mark Dunzo* DATE: 5/22/05  
 CADD Filename: ...shf002.mxd
