

PHASING

PHASE I

STEP 1 - INSTALL WORK ZONE ADVANCE WARNING SIGNS ON HAMPTON RD (SR 1485). SEE RSD 1101.01, SHEET 3 OF 3.

STEP 2 - USING RSD 1101.02, SHEET 1 OF 15 AS NEEDED, BEGIN CONSTRUCTION OF THE FOLLOWING PROPOSED ROADWAY SECTIONS UP TO, BUT NOT INCLUDING, THE FINAL LAYER OF SURFACE COURSE:

- L- STA 11+50+/- TO -L- STA 29+50+/- (SEE TMP-4 AND TMP-5)
- DR1- SEE TMP-5
- DR2- SEE TMP-5

- USING RSD 1101.02, SHEET 1 OF 15, CONDUCT THE FOLLOWING OPERATIONS IN A CONTINUOUS MANNER:

- A - REMOVE EXISTING GUARDRAIL ON LEFT SIDE OF HAMPTON RD.
- B - CONSTRUCT TEMPORARY PAVEMENT UP TO EDGE AND ELEVATION OF EXISTING PAVEMENT (SEE TMP-4, TMP-5 AND ROADWAY PLANS).
- C - INSTALL PCB AS SHOWN ON TMP-4 AND TMP-5. (SEE TMP-2A)

STEP 3 - BEHIND PCB, INSTALL TEMPORARY SHORING IN THE FOLLOWING LOCATIONS:

- L- 21+03+/- TO 21+25+/-, 25' RT (SEE TMP-2B FOR DATA)
- L- 22+79+/- TO 22+99+/-, 27' RT (SEE TMP-2B FOR DATA)

STEP 4 - USING RSD 1101.02, SHEET 1 OF 15 AS NEEDED, CONSTRUCT THE PROPOSED STRUCTURE. SEE TMP-4 AND TMP-5.

PHASE II

STEP 1 - USING RSD 1101.02, SHEET 1 OF 15, PERFORM THE FOLLOWING IN A CONTINUOUS MANNER AS SHOWN ON SHEETS TMP-6 AND TMP-7:

- A - COMPLETE CONSTRUCTION OF THE PROPOSED ROADWAY SECTION WITH TEMPORARY SLOPES WHERE PROPOSED UP TO, BUT NOT INCLUDING, THE FINAL SURFACE LAYER.
- B - PLACE TEMPORARY PAVEMENT MARKINGS AND PAVEMENT MARKERS IN THE FINAL PATTERN AND REMOVE CONFLICTING MARKINGS.
- C - PLACE TRAFFIC CONTROL DEVICES AS SHOWN AND SHIFT TRAFFIC TO THE FINAL PATTERN.



STEP 2 - USING RSD 1101.02, SHEET 1 OF 15 AS NEEDED, COMPLETE THE FOLLOWING:

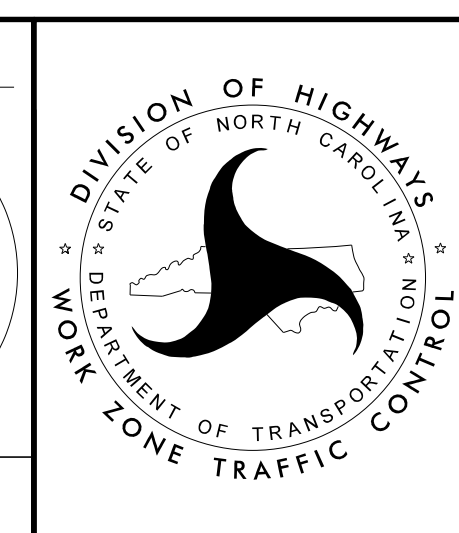
- REMOVE PCB INSTALLED IN PHASE I.
- REMOVE THE EXISTING STRUCTURE.
- REMOVE EXISTING PAVEMENT AS INDICATED IN THE ROADWAY PLANS.
- COMPLETE ALL PROPOSED ROADWAY CONSTRUCTION UP TO BUT NOT INCLUDING THE FINAL SURFACE LAYER.

STEP 3 - USING RSD 1101.02, SHEET 1 OF 15, COMPLETE THE FOLLOWING:

- A - PLACE THE FINAL LAYER OF SURFACE COURSE.
- B - PLACE THE FINAL PAVEMENT MARKINGS AND MARKERS AS SHOWN IN THE PAVEMENT MARKING PLANS.

STEP 4 - REMOVE ALL TRAFFIC CONTROL DEVICES.

APPROVED: 
DATE: 3/21/2017

DOCUMENT NOT CONSIDERED FINAL UNLESS ALL SIGNATURES COMPLETED



PHASING
