

PROJ. REFERENCE NO.	SHEET NO.
B-5694	TMP-3

# PHASING

NOTE: MAINTAIN ACCESS TO DRIVEWAYS AT ALL TIMES.

## PHASE 1

- STEP 1: USING RSD 1101.01, SHEET 3 OF 3. INSTALL WORK ZONE ADVANCE WARNING SIGNS
- STEP 2: USING RSD 1101.02, SHEET 1 OF 14, CONSTRUCT -DET-.


## PHASE 2



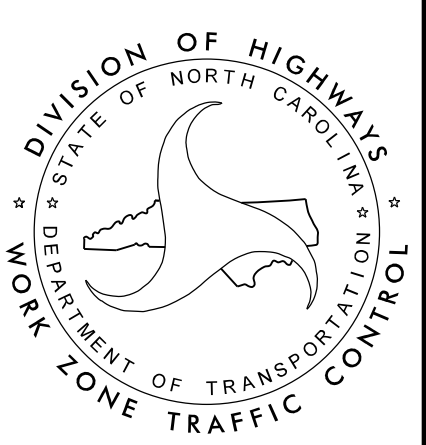
- STEP 1: USING RSD 1101.02, SHEET 1 OF 14, WEDGE TIE-INS OF -DET-, PLACE TEMPORARY PAVEMENT MARKINGS AND TRAFFIC CONTROL DEVICES USING RSD 1101.03, SHEET 3 OF 9. SHIFT 2 LANE, 2 WAY TRAFFIC ONTO DETOUR.
- STEP 2: CONSTRUCT -L- (NC 11) UP TO BUT NOT INCLUDING THE FINAL LAYER OF SURFACE COURSE FROM STA 17+00± TO STA 28+25±.

## PHASE 3

- STEP 1: CONSTRUCT -L- (NC 11) UP TO BUT NOT INCLUDING THE FINAL LAYER OF SURFACE COURSE FROM STA. 15+00± TO STA. 17+00± AND STA. 28+25± TO STA. 30+05.22± USING RSD 1101.02, SHEET 1 OF 14.
- STEP 2: USING RSD 1101.02, SHEET 1 OF 14 PLACE TEMPORARY PAVEMENT MARKINGS ON -L- FROM STA. 15+00.00. TO STA 30+05.22.  
  
SWITCH TRAFFIC ONTO PROPOSED -L- IN A 2 LANE, 2 WAY TRAFFIC PATTERN.
- STEP 3: PLACE TYPE III BARRICADES AND DRUMS ON DETOUR (REFER TO TMP-4 FOR SETUP). REMOVE DETOUR AND TEMPORARY GUARDRAIL.
- STEP 4: USING RSD 1101.02, SHEET 1 OF 14, PLACE FINAL LAYER OF SURFACE COURSE AND FINAL PAVEMENT MARKINGS ON -L-.
- STEP 5: REMOVE ALL TRAFFIC CONTROL DEVICES.

\$\$\$\$\$SYTIME\$\$\$\$\$  
\$\$\$\$\$DGN\$\$\$\$\$  
\$\$\$\$\$USERNAME\$\$\$\$\$



APPROVED:  DATE: 4/4/2022  SEAL			<h1 style="font-size: 2em;">PHASING</h1>
---	---	---	--
