

PHASE I CONTINUED

SECTION 1 - -L- STA 465+00 TO STA 650+00, -Y4- AND -Y5

3. BEHIND BARRIER, BEGIN CONSTRUCTION OF TEMPORARY PAVEMENT AT THE FOLLOWING:
 - * LOCATION S1-29 (OUTSIDE SHOULDER OF SB -L-) AS SHOWN ON TMP-16 AND TMP-17
 - * LOCATION S1-27 (OUTSIDE SHOULDER OF NB -L-) AS SHOWN ON TMP-17
 4. USING RSD 1101.02, SHEET 4 OF 14 AS NEEDED:
 - * PLACE TEMPORARY PCB AND CRASH CUSHION ON THE INSIDE SHOULDER OF SB -L- (TEMPORARY PAVEMENT LOCATION S1-23) FROM STA 635+00+/- AS SHOWN ON TMP-15 THRU TMP-17, and TMP-134G
 - * PLACE TEMPORARY PCB ON INSIDE SHOULDER OF NB -L- (TEMPORARY PAVEMENT LOCATION S1-26) AS SHOWN ON TMP-16, TMP-17 AND TMP-134G
 - * BEGIN CONSTRUCTION OF TEMPORARY PAVEMENT (INSIDE SHOULDER OF SB -L-) AT LOCATION S1-23 FROM STA 635+00+/- TO STA 628+36+/- AND AT LOCATION S1-22 AND EXTEND TEMPORARY PCB AS SHOWN ON TMP-13, TMP-14, TMP-14C, TMP-15 AND TMP-16 (NOTE: REMOVE ONLY AS MUCH EXISTING SHOULDER AS CAN BE REPLACED IN ONE WORK PERIOD)

USING RSD 1101.02, SHEETS 4 AND 9 OF 14 AS NEEDED, PLACE TEMPORARY PCB ON OUTSIDE SHOULDER OF NB -L- AS NEEDED TO INSTALL 36" PIPES ACROSS I-95 (TMP-16 AND TMP-17) IN A TRENCHLESS MANNER
 6. BEHIND BARRIER, CONSTRUCT TRENCHLESS DRAINAGE CONSTRUCTION OF DRAINAGE ACROSS I-95 NEAR STA 642+37+/- (NOTE: ANCHOR TEMPORARY PCB AS NEEDED ALONG THE SHOULDERS OF -L- AT THE TRENCHLESS SITE. SEE TMP-2TS1)
 7. USING RSD 1101.02, SHEET 4 AND 9 OF 14 AS NEEDED, REMOVE TEMPORARY PCB FROM THE OUTSIDE SHOULDER OF NB -L- FROM STA 640+52+/- TO STA 644+53+/- (TMP-16 & TMP-17)
 8. USING RSD 1101.02, SHEET 4 OF 14 AS NEEDED, COMPLETE CONSTRUCTION OF TEMPORARY PAVEMENT ON THE INSIDE SHOULDER OF SB -L- AT LOCATION S1-23 FROM STA 635+00+/- TO STA 628+36+/- AND LOCATION S1-22 AND EXTEND TEMPORARY PCB AS SHOWN ON TMP-14C, TMP-15 AND TMP-16 (NOTE: REMOVE ONLY AS MUCH EXISTING SHOULDER AS CAN BE REPLACED IN ONE WORK PERIOD)
- BEHIND BARRIER, COMPLETE CONSTRUCTION OF TEMPORARY PAVEMENT AT THE FOLLOWING:
- * LOCATION S1-29 (OUTSIDE SHOULDER OF SB -L-) AS SHOWN ON TMP-16 AND TMP-17
 - * LOCATION S1-27 (OUTSIDE SHOULDER OF NB -L-) AS SHOWN ON TMP-17
- USING RSD 1101.04, SHEETS 4 AND 9 OF 14, CONSTRUCT TEMPORARY PAVEMENT LOCATION S1-25 (OUTSIDE SHOULDER OF SB -L-) AS SHOWN ON TMP-15 THRU TMP-17

SECTION 2 - -L- FROM STA 650+00 TO STA 915+07, -Y1B-, -Y6- AND -Y7-


PHASE I, SECTION 1, STEP 3 CONTINUED ON TMP-3E

PLANS PREPARED FOR THE NCDOT BY:

M MOTT MACDONALD I & E, LLC
1101 HAYNES STREET, SUITE 101
RALEIGH, NC 27604


M MOTT MACDONALD NC LICENSE NO. F-0669

APPROVED: *Lori D. Stoucho*
DATE: 4/29/2022



**DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED**


APPROVED: *J.W. Woolard, Jr.*
DATE: 4/29/2022



**DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED**



Stantec Consulting Services Inc.
801 Jones Franklin Road
Suite 300
Raleigh, NC 27606
Tel. 919.851.6866
Fax. 919.851.7024
www.stantec.com
License No. F-0672

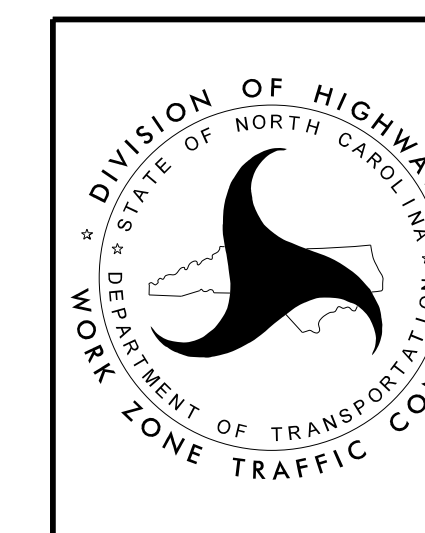

**TEMPORARY TRAFFIC CONTROL
PHASING
PHASE I**

3/28/2022
 G:\50100191\NV5_1-5987B\TrafficControl\Twp\200_071\I-5987B_TMP-3D_Phase I_220315.dgn
 User:ST086227
